


Activity ID	Activity Name	Original Duration	Remaining Duration	Schedule % Complete	Start	Finish	Qtr 1, 2021				
							Dec	Jan	Feb	Mar	Apr
UHLAND CITY OF UHLAND - S. OLD SP.							28-Feb-21, UHLAND CITY OF UHLAND				
UHLAND.S1 SITE 1 (3 PIPE CROSSING)							05-Feb-21, UHLAND.S1 SITE 1 (3 PIPE CROSSING)				
10	MOBILIZATION	1	1	0%	30-Nov-20	30-Nov-20					
20	TRAFFIC CONTROL	1	1	0%	01-Dec-20	01-Dec-20					
30	EROSION CONTROL	1	1	0%	02-Dec-20	02-Dec-20					
40	SITE PREP	3	3	0%	03-Dec-20	05-Dec-20					
50	EXCAVATION & DEMO	5	5	0%	06-Dec-20	10-Dec-20					
60	PIPE INSTALLATION (3 PIPE)	9	9	0%	11-Dec-20	19-Dec-20					
70	CONCRETE HEADWALLS (3 PIPE)	10	10	0%	20-Dec-20	29-Dec-20					
80	BACKFILL	3	3	0%	30-Dec-20	01-Jan-21					
90	INSTALLATION OF PIPE (1 PIPE)	2	2	0%	02-Jan-21	03-Jan-21					
100	CONCRETE HEADWALL (1 PIPE)	2	2	0%	04-Jan-21	05-Jan-21					
110	ROCK RIPRAP	3	3	0%	06-Jan-21	08-Jan-21					
120	ASPHALT & CONCRETE REPAIR	8	8	0%	12-Jan-21	19-Jan-21					
130	HANDRAIL	5	5	0%	22-Jan-21	26-Jan-21					
140	GUARDRAIL	8	8	0%	29-Jan-21	05-Feb-21					
UHLAND.S2 SITE 2 (1 PIPE CROSSING)							20-Feb-21, UHLAND.S2 SITE 2 (1 PIPE CROSSING)				
150	TRAFFIC CONTROL	1	1	0%	06-Feb-21	06-Feb-21					
160	EROSION CONTROL	1	1	0%	07-Feb-21	07-Feb-21					
170	SITE PREP	2	2	0%	08-Feb-21	09-Feb-21					
180	EXCAVATION & DEMO	2	2	0%	10-Feb-21	11-Feb-21					
190	INSTALLATION PIPE (3 PIPE)	3	3	0%	12-Feb-21	14-Feb-21					
200	CONCRETE HEADWALLS (3 PIPE)	2	2	0%	15-Feb-21	16-Feb-21					
210	BACKFILL	2	2	0%	17-Feb-21	18-Feb-21					
220	ASPHALT & CONCRETE REPAIR	2	2	0%	19-Feb-21	20-Feb-21					
UHLAND.PO PUNCH OUT							28-Feb-21, UHLAND.PO PUNCH OUT				
A1000	REMOVE EROSION CONTROLS	5	5	0%	21-Feb-21	25-Feb-21					
A1010	REMOVE SIGNS & BARRICADES	3	3	0%	26-Feb-21	28-Feb-21					

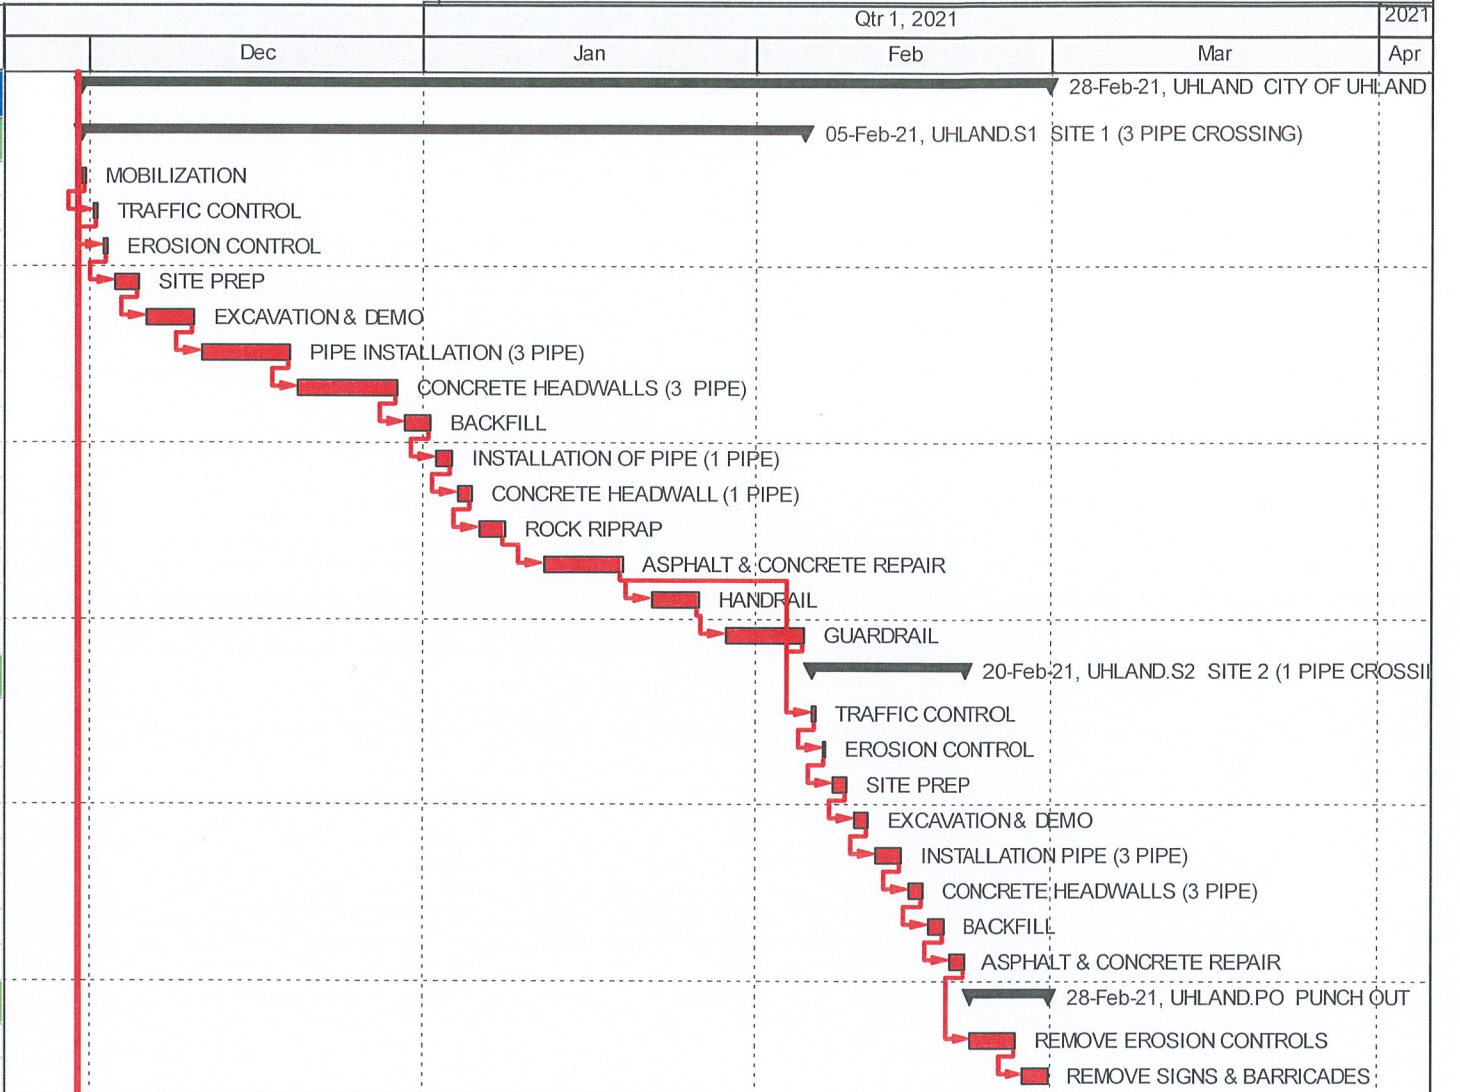

█ Actual Level of Effort
 █ Remaining Work
 ◆ Milestone
█ Actual Work
 █ Critical Remaining Work
 ▸ summary
